



VSF PROJECTS LIMITED

A MULTI PRODUCT FREE TRADE WAREHOUSING ZONE WITH INLAND CONTAINER DEPOT

Project Location:

**Sy 782 to 1236, Ankulapaturu Village, chillakur Mandal, Tirupati
District, Andhra Pradesh-524412**




Warehouse 1 = 3,60,000SFT

MARCH 2025 REPORT

www.vsfproject.com



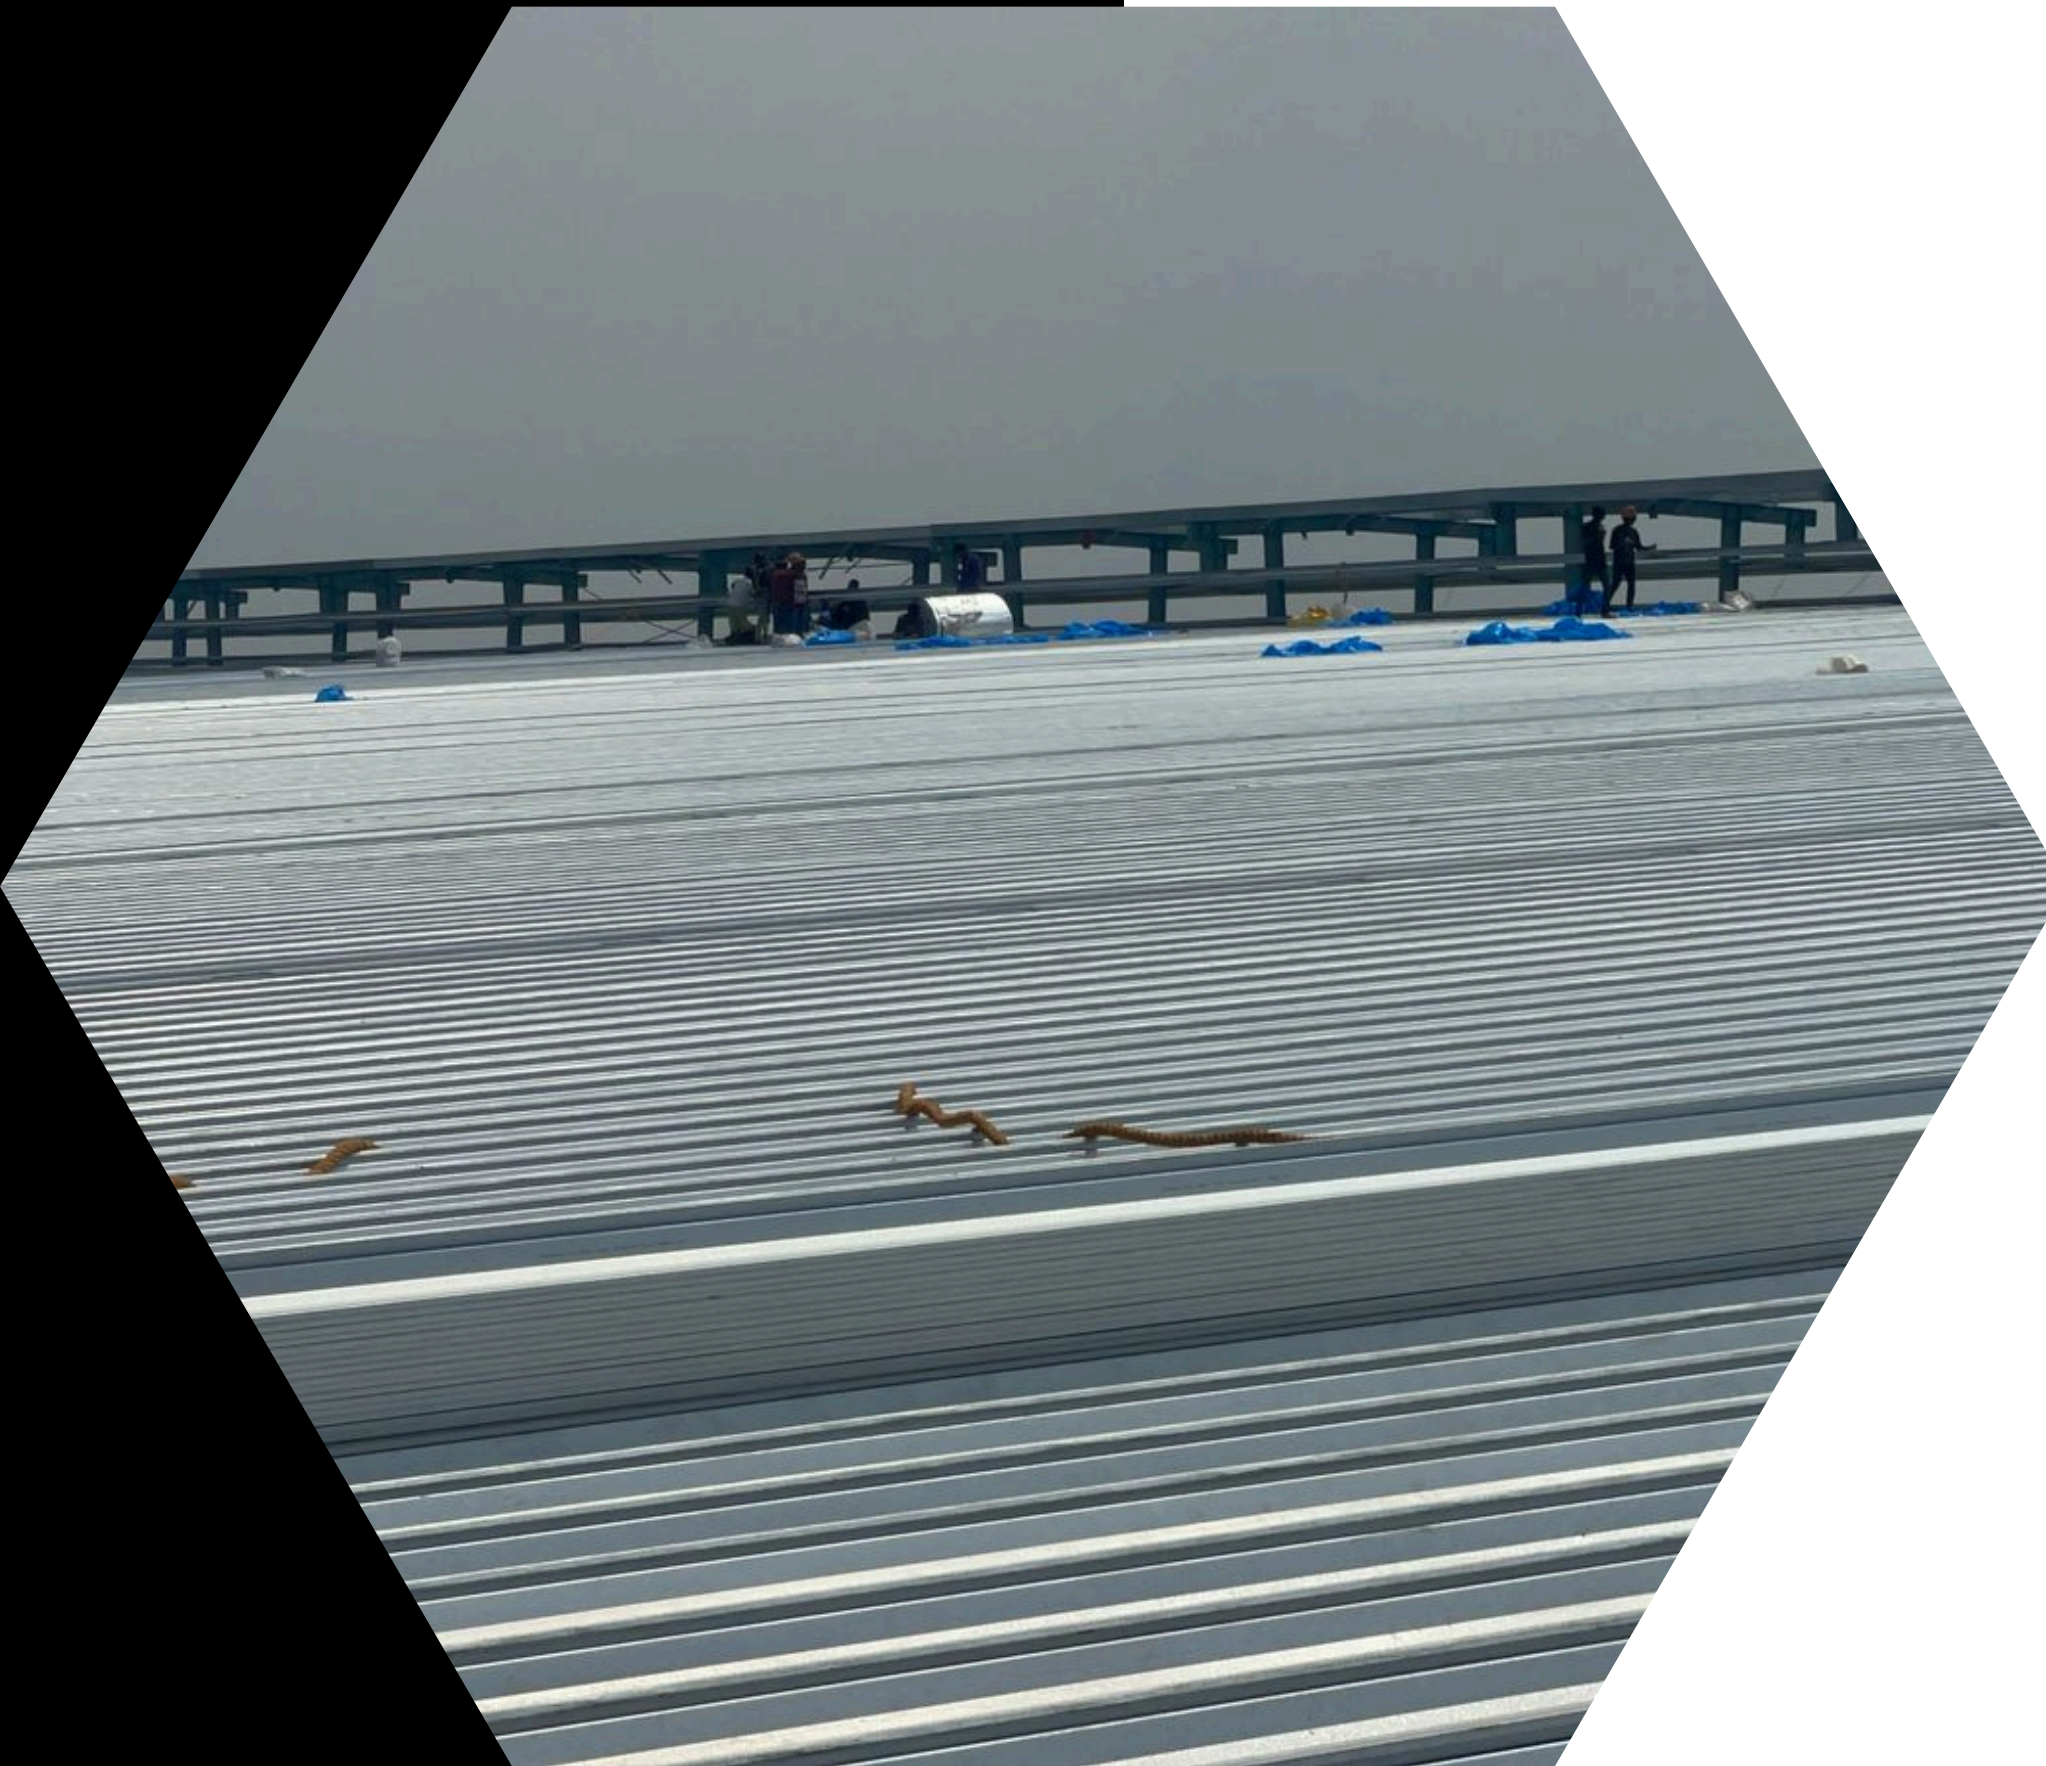

Insulation Work and Roof Sheeting work in under progress

Our Dedicated Team of 32 skilled members are actively Erecting the Warehouse each day. Their Coordinated efforts and commitment to excellence are driving continuous progress, ensuring with precision and efficiency.

On Going Warehouse 1 Civil Work

Executing the Warehouse brick work meticulously, ensuring solid and durable structure.

Concurrently, the construction of rolling shutter columns is in progress.

Additionally, work on the Dock
Levellers is moving forward ,aiming at
streamlining loading and unloading
operations





Mobilized Dock Levellers

We have successfully mobilized the dock levellers for warehouse 1, marking a critical milestone in this month



**90% of the Warehouse 1
VDF Flooring Completed
as of 31st March 2025.**



Laying of Electrical Cable inside the warehouse is in progress



Our Team is engaged in laying of Hume Pipes and Cables inside and around this Grade A Warehouse .This Work is Pivotal in establishing a resilient Infrastructure that supports both current and Future Operational Needs

APPROACH ROAD PROGRESS



BT ROAD

FORMATION OF ANOTHER 1.1KM
BT ROAD OF APPROACH ROAD
HAS BEEN COMPLETED IN THE
MONTH OF MARCH 2025



WETMIX

LAYING OF WETMIX
FOR ANOTHER
700MTRS IS IN
PROGRESS.



CAUSEWAY

RETAINING WALL OF
CAUSE WAY IS IN
PROGRESS



WWW.VSFPROJECT.COM



ADMIN BUILDING

We have completed the Wall Care and Premier Coating of Paints.

Completed Laying of Tiles and Installation of Ceiling is executed.

Notably, 80% of Electrical Work has been completed in this budling.



CUSTOMS BLOCK



- 1. Wall care and Premier Coating of paints completed***
- 2. Plumbing and Fixing of Sanitary is under progress***
- 3. 90% of Electrical Work is completed***



CANTEEN BLOCK & ACCOMIDATION

- 90% of Canteen Electrical Work is completed and vendor rooms electrical work is under progress.
- Fixing of Windows and doors are under progress
- Wall Care and Painting works are under progress
- Plumbing and fixing of sanitary are under progress
- Laying of Tiles is under progress.





















Thank You
